Attachment 5
Project Schedule

ID	Task Name	Duration	Start	Finish
1	Project Administration	460 days	Mon 6/6/11	Fri 3/8/13
2	Labor Compliance	360 days	Fri 9/30/11	Thu 2/14/13
3	Reporting	336 days	Fri 11/25/11	Fri 3/8/13
4	Land Purchase/Easement	120 days	Fri 4/15/11	Thu 9/29/11
5	Assessment and Evaluation	60 days	Fri 4/15/11	Thu 7/7/11
6	Environmental Documentation	120 days	Fri 5/27/11	Thu 11/10/11
7	Final Design	80 days	Fri 8/5/11	Thu 11/24/11
8	Permitting	100 days	Fri 7/8/11	Thu 11/24/11
9	Construction Contracting	60 days	Fri 11/25/11	Thu 2/16/12
10	Construction Administration	240 days	Fri 2/17/12	Thu 1/17/13
11	Mobilization and Site Preparation	10 days	Fri 2/17/12	Thu 3/1/12
12	Project Construction	239 days	Fri 3/2/12	Wed 1/30/13
13	Performance Testing and Demobilization	210 days	Fri 4/27/12	Thu 2/14/13
14	Environmental Compliance/Mitigation/ Enhancement	200 days	Fri 2/17/12	Thu 11/22/12

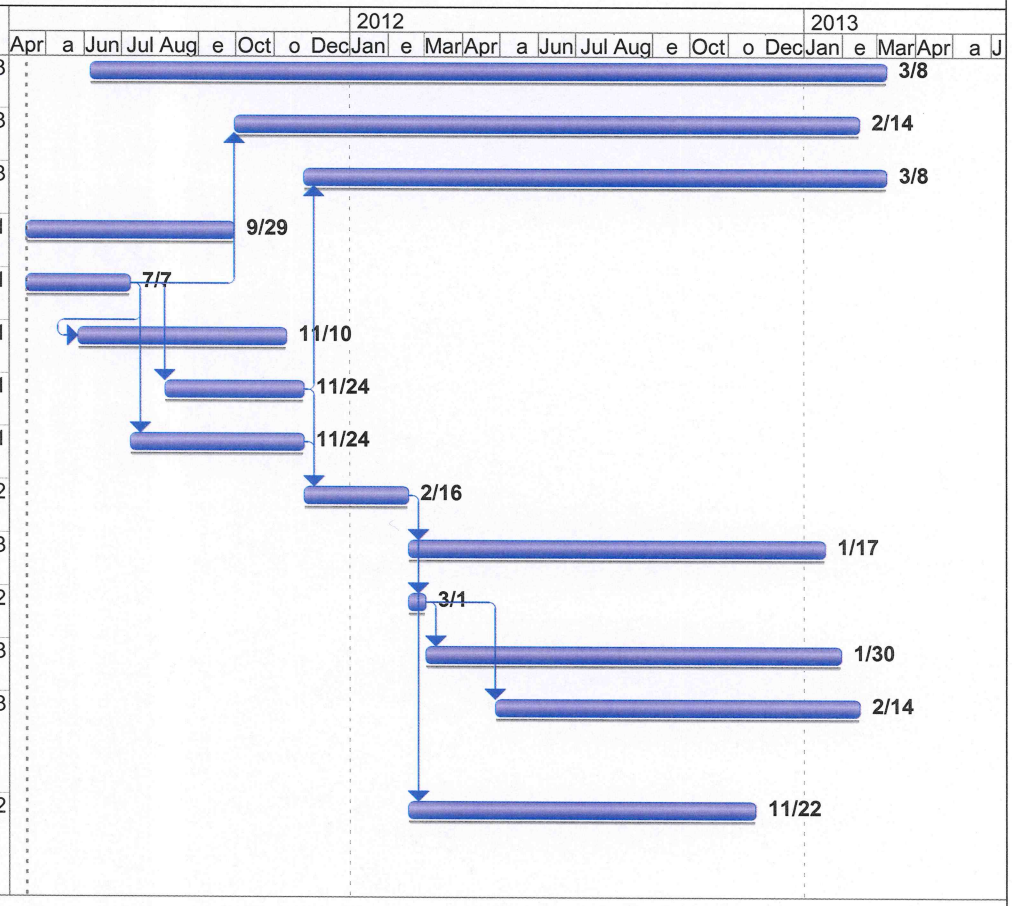

Project: Project Schedule
Date: Fri 4/15/11

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
